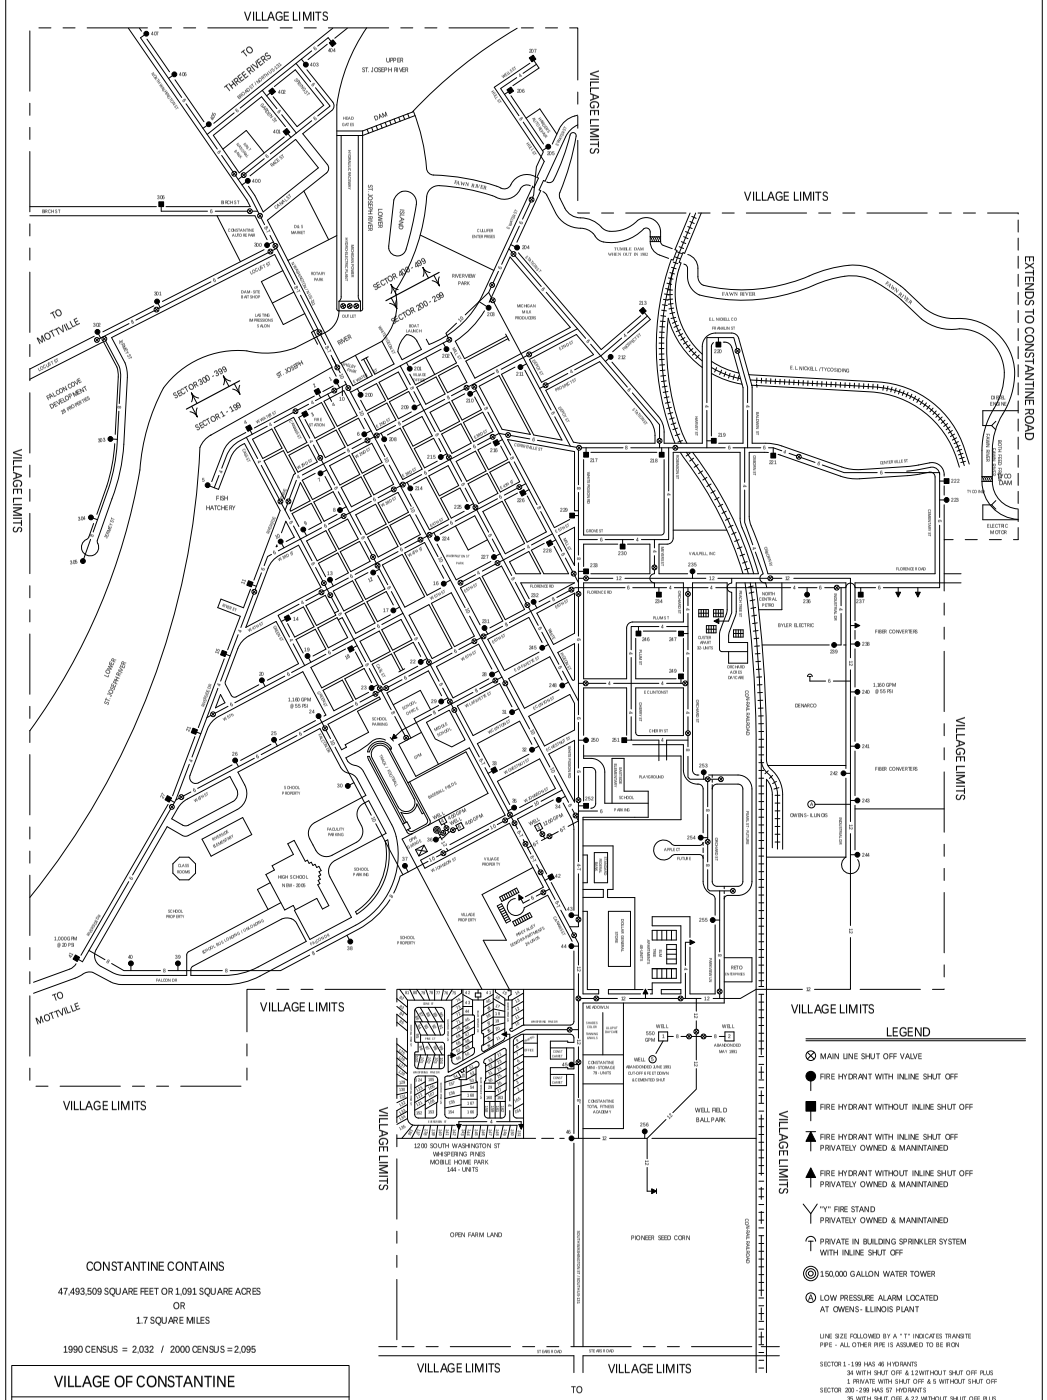

LEGEND

- MAIN LINE SHUT OFF VALVE
- FIRE HYDRANT WITH INLINE SHUT OFF
- FIRE HYDRANT WITHOUT INLINE SHUT OFF
- FIRE HYDRANT WITH INLINE SHUT OFF PRIVATELY OWNED & MANINTAINED
- FIRE HYDRANT WITHOUT INLINE SHUT OFF PRIVATELY OWNED & MANINTAINED
- "Y" FIRE STAND PRIVATELY OWNED & MANINTAINED
- PRIVATE IN BUILDING SPRINKLER SYSTEM WITH INLINE SHUT OFF
- 150,000 GALLON WATER TOWER
- LOW PRESSURE ALARM LOCATED AT OWENS - ILLINOIS PLANT

LINE SIZE FOLLOWED BY A "T" INDICATES TRANSITE PIPE - ALL OTHER PIPE IS ASSUMED TO BE IRON

SECTOR 1 - 199 HAS 46 HYDRANTS
34 WITH SHUT OFF & 12 WITHOUT SHUT OFF PLUS
1 PRIVATE WITH SHUT OFF & 5 WITHOUT SHUT OFF
SECTOR 200 - 299 HAS 57 HYDRANTS
35 WITH SHUT OFF & 22 WITHOUT SHUT OFF PLUS
7 PRIVATE HYDRANTS AND 2 "Y" FIRE STANDS
SECTOR 300 - 399 HAS 7 HYDRANTS
6 WITH SHUT OFF & 1 WITHOUT SHUT OFF
SECTOR 400 - 499 HAS 8 HYDRANTS
5 WITH SHUT OFF & 3 WITHOUT SHUT OFF

TOTAL NUMBER OF HYDRANTS IS 131
TOTAL NUMBER OF PRIVATE HYDRANTS IS 14
TOTAL NUMBER OF "Y" FIRE STANDS IS 2

TOTAL WELL PUMPING CAPACITY IS 2,550 GPM

CONSTANTINE CONTAINS

47,493,509 SQUARE FEET OR 1.091 SQUARE ACRES
OR
1.7 SQUARE MILES

1990 CENSUS = 2,032 / 2000 CENSUS = 2,095

VILLAGE OF CONSTANTINE		
WATER SYSTEM MAP		
DATE JAN 3, 2005	SCALE 1" = 350'	DRAWN BY SHELBY W. NICKELL
PREPARED FOR THE PEOPLE OF CONSTANTINE		
